


ID	Task Name	Duration	Q2 '01			Q3 '01			Q4 '01			Q1 '02			Q2 '02			Q3 '02			Q4 '02			Q1 '03			Q2 '03			Q3 '03			Q4 '03			Q1 '04			Q2 '04		
			A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J
1	request samples AVT (1) (pigtailed)	1 day																																							
2	fibre, ribbon and cable contract signed (1 day																																							
3	fibre AVT (1) sample delivery	70 days																																							
4	AVT (1) gammas	15 days																																							
5	AVT (1) neutrons	15 days																																							
6	AVT(1) clearance	1 day																																							
7	validation of buffered fibre	40 days																																							
8	test labels	30 days																																							
9																																									
10	production of buffered fibre	31 days																																							
11	lot acceptance of buffered fibre	10 days																																							
12	validation of final buffered fibre	40 days																																							
13																																									
14	MU-connector contract signed (C2)	1 day																																							
15																																									
16	request MU PP batch(1) and LD AVT(1,	1 day																																							
17	MU PP batch (1) delivery, 2%	84 days																																							
18	MU delivery for laser AVT(1)	35 days																																							
19	MU PP lot acceptance (for LD PP)	10 days																																							
20	Qualify MU pre-prod	80 days																																							
21																																									
22	MU Q-Request batch (2)	1 day																																							
23	MU batch (2) delivery, 8%	84 days																																							
24	MU batch (2) lot acceptance	10 days																																							
25																																									
26	MU Q-Request batch (3)	1 day																																							
27	MU batch (3) delivery, 15%	84 days																																							
28	MU batch (3) lot acceptance	10 days																																							
29																																									
30	MU Q-Request batch (4)	1 day																																							
31	MU batch (4) delivery, 15%	84 days																																							
32	MU batch (4) lot acceptance	10 days																																							
33																																									
34	MU Q-Request batch (5)	1 day																																							
35	MU batch (5) delivery, 15%	84 days																																							
36	MU batch (5) lot acceptance	10 days																																							



ID	Task Name	Duration	Q2 '01			Q3 '01			Q4 '01			Q1 '02			Q2 '02			Q3 '02			Q4 '02			Q1 '03			Q2 '03			Q3 '03			Q4 '03			Q1 '04			Q2 '04		
			A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J	J	A	S	O	N	D	J	F	M	A	M	J
37																																									
38	MU Q-Request batch (6)	1 day																																							
39	MU batch (6) delivery, 15%	84 days																																							
40	MU batch (6) lot acceptance	10 days																																							
41																																									
42	MU Q-Request batch (7)	1 day																																							
43	MU batch (7) delivery, 15%	84 days																																							
44	MU batch (7) lot acceptance	10 days																																							
45																																									
46	MU Q-Request batch (8)	1 day																																							
47	MU batch (8) delivery, 15%	84 days																																							
48	MU batch (8) lot acceptance	10 days																																							
49																																									
50	LD contract signed (C3)	1 day																																							
51																																									
52	LD request samples AVT (1)	1 day																																							
53	LD AVT (1) sample delivery	112 days																																							
54	LD AVT (1) irradiation	58 days																																							
55	LD AVT (1) de-activation then ageing	70 days																																							
56	LD AVT (1) advance clearance	1 day																																							
57	LD AVT (1) final clearance	1 day																																							
58																																									
59	LD Request samples AVT (2)	1 day																																							
60	LD AVT (2) sample delivery	112 days																																							
61	LD AVT (2) irradiation	58 days																																							
62	LD AVT (2) de-activation then ageing	70 days																																							
63	LD AVT (2) advance clearance	1 day																																							
64	LD AVT (2) final clearance	1 day																																							
65																																									
66	LD Request samples AVT (3)	1 day																																							
67	LD AVT (3) sample delivery	112 days																																							
68	LD AVT (3) irradiation	58 days																																							
69	LD AVT (3) de-activation then ageing	70 days																																							
70	LD AVT (3) advance clearance	1 day																																							
71	LD AVT (3) final clearance	1 day																																							
72																																									

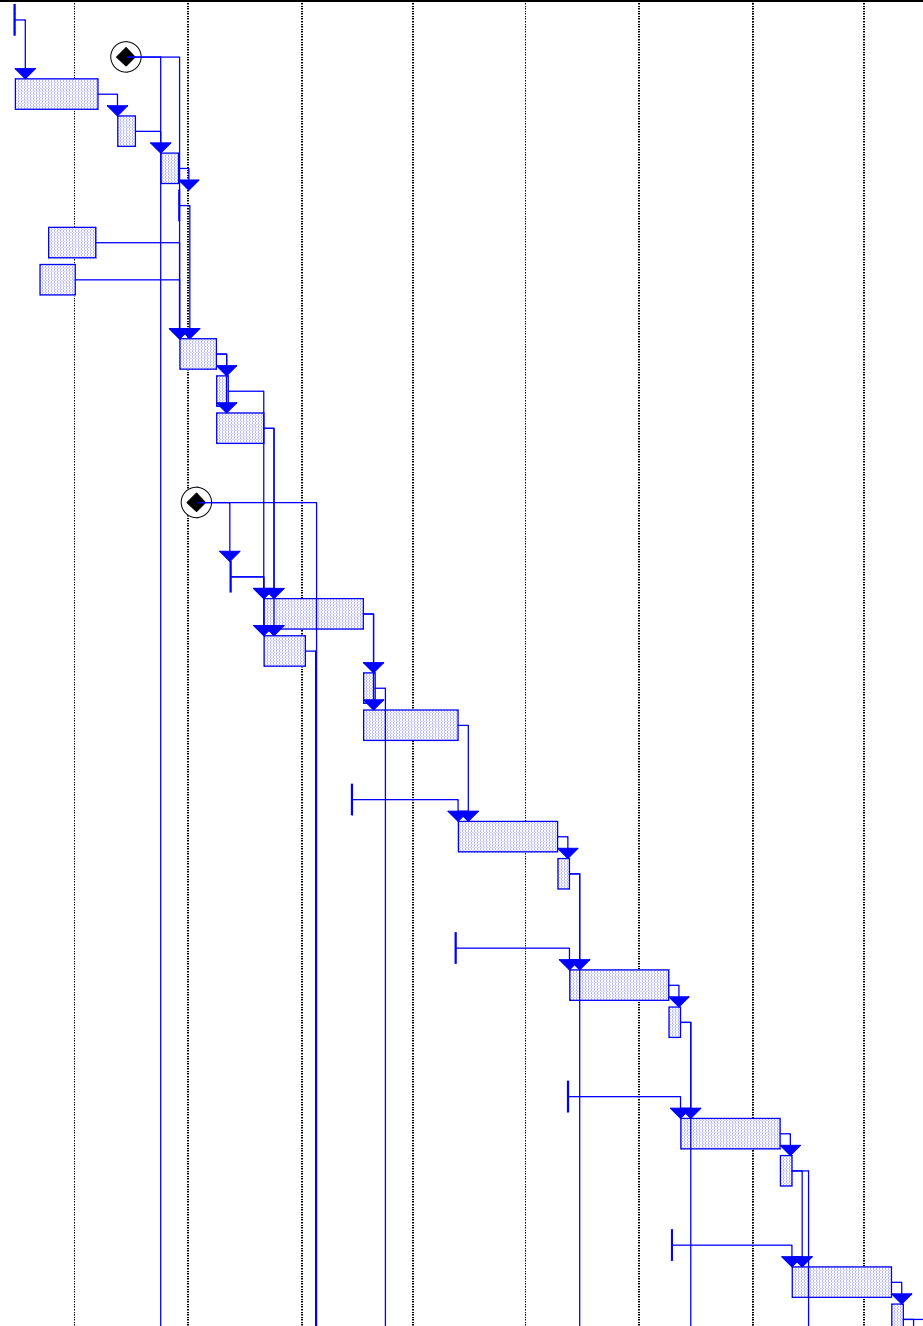
